BPC REPORT

FACULTY SENATE FEBRUARY 3, 2005

Contents

- Overview of Capital Projects
- Generic SUCF Project Timeline
- Estimated Timeline for Academic Village
- SEMPRA Timeline
- Academic Village Comfort & Air Quality
- Proposal for a Strategic Plan 2006-2011
- Proposal for Faculty Membership ON BPC

CAPITAL PLAN OVERVIEW 02/04/2004

Contents

- 1. Overview of Revenues and Project Costs
- 2. Breakdown of Academic Village Projects
- 3. Timeline on the process of implementing capital projects

In 2003 the College was informed that the 2003-2008 Capital Plan would be changed to 2004-2009 by State Construction Fund. Over the 2003-04 BPC worked on defining projects and moved to the Request For Qualifications phase in several projects.

Current Capital Projects will be funded from several sources. The largest component of the funds is the approximately \$20 million allocated to the campus for the years 2004-2009. The timing for release of those funds remains a question. The \$20 million represents a \$6 million increase over the original amount awarded to the campus. However an additional

REVENUES	
Capital Plan 04-09	\$20,000,000.00
Training Facility	\$10,298,000.00
Matching Funds	\$1,544,326.00
M & R	\$200,700.00
10	32,043,026.00

year was also added to the plan. The Academic Village is to receive the biggest part of the Capital Plan 04-09 revenues.

PROJECTS IN CONSTRUCTION PHASE

\$9,000,000

At the moment we have committed 9,329,000 of those funds to projects designed during the prior capital

plan. Among those projects in the construction phase are repaving of the campus roadways and paths, campus signs, terraces and roof repairs of the Academic Village and a one time allocation of 3.5 million to the SEMPRA energy project.

CURRENT EXPENDITURES		Phase
SEMPRA	\$3,500,000.00	Active
Replace Service Group Roofs	\$578,000.00	Active
ADA Paths/Sidewalks/Roads Paving	\$1,851,000.00	Active Summer 04
AV Aprons/Terraces/Roofs	\$1,892,000.00	Bid & Construction Spring 05
Campus Signage	\$500,000.00	Active
Y		
TOTAL	\$8,321,000.00	

In 2003 the BPC recommended to the President that with the training facility funds not being allocated to a new academic building the Academic Village's interior and exterior would be the focus of those funds.

\$1,851,000.00 dollars has been allocated to campus roads and path repaving, These projects are in the construction phase during years 2004-05.

\$1,892,000.00 is dedicated to the Academic Village roofs, terraces and paths. This should address the leaks in the A,B,C sections. Projected bid and construction is spring 2005.

Update: Spring 2005

Most campus roadways and paths have been completed as of the summer 2004. Additional work will be done on steps along the paths and the path to the new dorms in Spring 2005. The campus signage design is completed construction will begin soon.

PROJECTS IN THE INITIAL PHASE

\$9,500,000

The College is in the beginning phases of three projects. In each case a Request for Qualifications (RFQ) was undertaken. Presently, we have received the Request for Qualifications (RFQ) for the Academic Village interior, facades for Academic Village and the Campus Center, as well as data wiring for the interiors of the campus buildings. We have chosen designers for Academic Village interior rehab and the College has just received approval to begin the design phase. Assuming no SUCF follows through architects will be interviewing campus constituents and designing in the spring semester. We will require SUCF's approval to go ahead with the construction phase.

Campus Wiring

Campus network wiring will be upgraded to current standards, providing improved network performance and new options in negotiating our telephone contract in two years. One hoped for objective is to realize savings with our current telephone vendor or to move to a cheaper data oriented telephone service.

Classroom Upgrades

Classrooms in the Academic Village, Science Building and several in the Campus Center will receive renovations including light fixtures. removal of asbestos where necessary, podiums in presentation classrooms, new ceilings, electrical and data outlets consistent with presentation capability, and general esthetic upgrades.

Projects in the Initial Phase		Phase
Estimates		
Campus Wiring	\$850,000.00	Negotiating with Designers
AV Interiors Design	\$250,000.00	Approved 12/2004
Classrooms AV, Science, CC	\$3,750,000.00	
AV Public Spaces	\$1,500,000.00	
AV Facades	\$1,500,000.00	RFQ
Campus Center Exterior	\$1,650,000.00	
	\$9,500,000.00	

Academic Village public space including the pit, bathrooms and the D wing lounge will also receive renovations under this proposal.

Facades

We are proceeding with a design of facades for the Academic Village, and Campus Center. The above represents the order of priority and rough estimation of costs. At a minimum we believe we will be able to resurface the Academic Village and the front of the Campus Center with a Textured Coating.

PROJECTS IN PLANNING PHASE

\$9,000,000

This semester the Capital Subgroup will prioritize the planning of two projects for the Campus Center: one, a general renovation of interior areas now in disrepair- walls, bathrooms, and flooring in a number of high traffic areas are unsightly and need repair- and two, the old bookstore. — constructing a space for bursar and financial aid.

Projects in Planning Phase		
Bookstore	\$1,500,000.00	Design
Backup Generators (3)	\$750,000.00	Defining
Fire Alarm and Cable Pulls		Defining
Electrical Switcher	\$750,000.00	Defining
Campus Center Renovations	\$1,000,000.00	Defining
Science Building Lobby Ceiling & Leaks		Defining
Subtotal	4,000,000.00	

Other potential work in the Campus Center could include some renovations to registrar front window and office space vacated by financial aid, rehab of Visual Arts studios and gallery.

Submitted by Thomas DelGiudice Vice Chair on behalf of the BPC

Beyond the Campus Center the campus needs repair the fire alarm and provide for a fire suppression system in Computing Services.

The committee also agreed that an assessment of the needs and future use of the library should be undertaken with the eventual result a major design renovation. The committee has not had enough time to assess other possibilities but will continue to do so.

CRITICAL MAINTENANCE

\$5,000,000

Basic infrastructure maintenance can be expensive and needs to be factored in to any allocation. Between \$4 and 5 million probably needs to be put aside for these purposes.

ACADEMIC VILLAGE PROJECTS

ROUGH BREAKOUT ACADEMIC			
VILLAGE			
	Estimated Costs	Phase	
SEMPRA	\$3,500,000*	Active	2004
Roofs, Terraces and Paths	\$1,892,000	Construction	Spring 05
Interiors Classrooms, Bathrooms, Public	\$5,500,000**	Design	Spring 05
Spaces			
Backup Generator	\$250,000		Spring 05
Data Wiring	\$750,000	Contracting/Design	Spring 05
Facades	\$1,500,000	RFQ	
TOTAL**	\$13,392,000		

 ^{*} allocated in 2003 for the SEMPRA energy project.

 ^{**}we allowed for flexibility by budgeting conservatively on other projects until we get better numbers on the actual costs from the architect/designer.

Estimated Timeline for Academic Village

December 2004 – January 2006 There are other projects that will be included in a more detail presentation by the President. The timelines below are contingent on timely turn around time by state offices where applicable.

Dece January August November		2004	2005	2004 2005 February- April		May June-	September	1	January 2006	
RAA AV Work s and Design Completed for Neetings Contract AV Roofs and Aprons How campus is affected? Campus community should hear soon. Negotiating Contract on Design Wiring hd one ris Negotiating Contract on Design for Academic Village for Horors. Design for Academic Village for Real with faculty and staff. Create Preliminary Drawings and then Contract on Depending March February Evaluate RFQs Design for Academic Village for Academic Village for Academic February Bid Contract Oppening March February Evaluate RFQs Design for Academic Village for Academic Village for Academic February Bid Contract Oppening March February February Evaluate RFQs Design March February Evaluate RFQs Design March February Fe		Dece	January				st			
s and Design Completed for Preconstructi Bid Opening Construction Roofs AV Roofs and Aprons On Meetings Contract and Aprons Is affected? Campus Community Should hear Soon. Wiring Miring Contract on Design For Academic Village Soons Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings and then Construction Drawings. Bid Contract Construction Drawings and then Construction Opening March February Soft Soons Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings and then Construction Drawings. Bid Contract Construction Construction Architect March Soons Soft Soons Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings.	SEMPRA	AV Wo	ork							
Is affected? Campus Community Soon. Negotiating Contract on Design Miring Niring Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Dopening Design March Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Opening Design March February March February	Aprons and		Design Completed for	Preconstructi	Bid Openir		uction Roofs			
bus Negotiating Contract on Design Wiring and hone ors Soon. Wiring Miring Contract on Design For Academic Village or Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Process Bid Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Process Bid Architect meet with faculty and staff. Create Preliminary Drawings. Bid Process Bid Architect meet with faculty and staff. Create Preliminary Drawings. February Architect meet With faculty and staff. Construction at the Construction of the Contract and Dependent of the Construction of the Con	NOOLS		AV NOOIS and Aprons	How campus is affected?	COULT	dina 				
bus Negotiating Contract on Design Wiring and hone ors Create Preliminary Drawings and then Construction Design for Academic Village then Construction Drawings. Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Drawings. Create Preliminary Drawings and then Construction Copening March Sebruary Architect Design Contract Construction Copening Architect Design Construction Copening Architect Design Contract Construction Copening Architect Construction Copening Architect Construction Copening Architect Construction Copening Architect Construction Copening Cop				Campus			14			
us Negotiating Contract on Design Wiring and whone ors rooms to make the contract on the contract of the Construction Drawings and then Construction Drawings. Bid Contract Construction Drawings and then Construction Drawings. Bid Contract Construction Prawings and then Construction Drawings. Bid Contract Construction Drawings. Bid Contract February March February Sand then Construction Drawings. Bid Contract Construction Drawings. Bid Contract Construction Drawings. Bid Contract Construction Drawings and then Construction Drawings.			8	community should hear						
us Negotiating Contract on Design Wiring and hone hone ors rooms construction brawings and staff. Create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Co				soon.						-
and hone ors Design for Academic Village Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Contract Pebruary Bid Contract Pebruary Bid Contract Pebruary Bid Contract Construction Drawings. Bid Contract Pebruary Bid Contract Construction Bid Sand Bid Contract Construction Bid Sand Bid Contract Pebruary February Febr	Campus		Negotiating Contract on	Design Wi	ring		Bid Process	Construct	ion	
and hone ors ors rooms vublic character up up rators ir of s and less lend lend lend Design for Academic Village Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Anchitect meet with faculty and staff. Create Preliminary Drawings and then Construction Opening March February Evaluate RFQs Design for Academic Village Bid Process Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Opening March February	Wiring		Wiring							
ors rooms rooms rooms rooms rublic ss and up rators rir of s and less rooms Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Opening March February February Rators Rebruary February Februa	Date and									
ors rooms rooms rooms rublic ubblic ss Architect meet with faculty and staff. Create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Opening March February iors ir of s and les	Telephone									
rooms vublic ess create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Opening March February iors ir of s and les	Interiors			Design for	Academic Vi	llage	Bid Process	Construct	ion	
Create Preliminary Drawings and then Construction Drawings. Bid Contract Construction Opening March February iors ir of s and les	Classrooms			Architect 1	neet with fact	ilty and staff.				
then Construction Drawings. Up Bid Contract Construction Opening March February February ir of s and les	and Public			Create Pre	liminary Drav	vings and				
up Bid Contract Construction rators Opening March February February iors Evaluate RFQs ir of Its and	Spaces			then Const	ruction Draw	ings.				_
rators Opening March February February iors ir of s and les	Backup			Bid	Contract	Construction	u			
iors February February Evaluate RFQs and Family Evaluate RFQs and February	Generators			Opening	March					
iors ir of s and				February						
Repair of Walls and New Facades	Exteriors					Evaluate RI	iQs	Design		
Walls and New Facades	Repair of									
New Facades	Walls and									
Facades	New									
	Facades									

GENERIC SUCF PROJECT TIMELINE


What appears below is rough list of steps that must be undertaken for each project. Assumptions:

- State legislature doesn't change allocation of Capital Funds. Such a circumstance occurred last year when the Capital Funds 2003-2008 was changed to 2004-2009 thereby putting the timeline on a year hold.
- 2. Office of State Controller doesn't hold up contract for unforeseen circumstance.
- 3. No state fiscal crisis occurs diverting resources on campus from working on such projects in a timely manner.
- 4. No major facility crisis occurs holding up the College's ability to execute on our end.

	STAGE		TIME PERIOD
	Define Project		(2 months)
	RQF for vendors of design.		(2 months)
	Send MOU for the project (new procedure	Need permission from SUCF	(2-3 months)
7	as of Sept 2004) for PERMISSION TO GO	to proceed on projects over	
(7)	AHEAD WITH DESIGN FROM SUCF	\$1 million threshold	
\subseteq	STATE CONSTRUCTION FUND		
DESIGN	Pick Vender for Design Negotiate Contract		(1 - 1.5 month)
Ш	Send Design Contract to SUCF, Attorney		(2-3 months)
	General and Office of the State Controller.		
	Design Phase	depending on the size of the	(4-6 months)
		project	
	Bid Process for Construction	assuming SUCF allows us to	(2 months)
w		run the project	
S	Negotiate a Contract with Construction		(1 - 1.5 month).
9	Vendor		
	Send Construction Contract to SUCF,		(2-3 months)
	Attorney General and Office of the State		
	Controller.		
.0			
ਹ			
\Box			
=======================================		SUBTOTAL	18 – 24 months
S			
Construction Phase	Actual Construction		
O			

ADDITIONAL INFORMATION REGARDING THE RESOLUTION HVAC CONDITIONS IN ACADEMIC VILLAGE

After doing some research into the sequence of events leading up to the problem of no air conditioning in Academic Village in the summer 2004, I submit the following timeline. There are supporting documents for much of what appears below. I submit this information in the interests of completing the narrative.

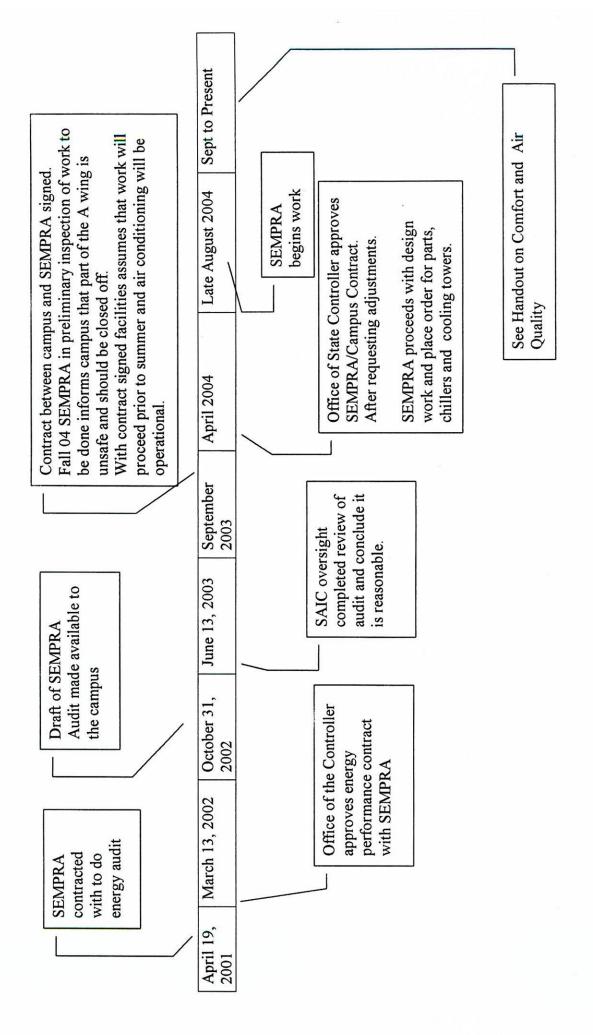

Submitted by Thomas DelGiudice Vice Chair on behalf of the BPC
